

沃港路路基左侧缺土方计算


序号	施工桩号	单位	横断面积m ²	平均横断面积m ²	长度m	缺土方m ³	备注
1	K0+43.685	m	2.228				K0+43.685~73.157左侧打木桩段
2	K0+060	m	5.083	3.656	16.315	59.639	
3	K0+080	m	4.538	4.811	20.000	96.210	
4	K0+100	m	0.640	2.589	20.000	51.780	
5	K0+120	m	5.127	2.884	20.000	57.670	K0+183.189~203.189三中沟桥
6	K0+140	m	6.708	5.918	20.000	118.350	
7	K0+160	m	7.614	7.161	20.000	143.220	
8	K0+180	m	7.016	7.315	20.000	146.300	
9	K0+204	m	10.789	8.903	3.200	28.488	
10	K0+220	m	6.507	8.648	16.000	138.368	
11	K0+260	m	4.830	5.669	37.000	209.735	
12	K0+280	m	6.645	5.738	20.000	114.750	
13	K0+300	m	0.581	3.613	20.000	72.260	
14	K0+320	m	3.881	2.231	20.000	44.620	
15	K0+340	m	0.330	2.106	20.000	42.110	
16	K0+360	m	0.773	0.552	20.000	11.030	
17	K0+380	m	5.472	3.123	20.000	62.450	K0+392.847~489.222左侧打木桩段
18	K0+400	m	6.808	6.140	20.000	122.800	
19	K0+420	m	7.992	7.400	20.000	148.000	
20	K0+440	m	7.315	7.654	20.000	153.070	
21	K0+460	m	7.394	7.355	20.000	147.090	
22	K0+480	m	8.554	7.974	20.000	159.480	
23	K0+500	m	7.483	8.019	20.000	160.370	
24	K0+520	m	7.427	7.455	20.000	149.100	
25	K0+540	m	7.519	7.473	20.000	149.460	
26	K0+560	m	6.988	7.254	20.000	145.070	
27	K0+580	m	6.245	6.617	20.000	132.330	
28	K0+600	m	8.167	7.206	20.000	144.120	
29	K0+620	m	8.320	8.244	20.000	164.870	K0+666~692盘裕河桥
30	K0+650	m	4.251	6.286	30.000	188.565	
31	左加宽20cm	m ³		1.241	582.515	723.134	86.25%
32	压实补偿	m ³		0.888	675.400	599.755	
合计缺土方量		m ³		未计入损耗		4684	压实方

注：1、沃港路路基全线两侧边坡全部按原设计1:1.5变更为1:1计算并实施。


2、如路基左侧河道加宽20cm压实宽度后还不稳定即不能正常上压路机碾压，则

缺土方量也另行相应增加。

测量：




复核：



现场监理：



沃港路道路路基横断面图

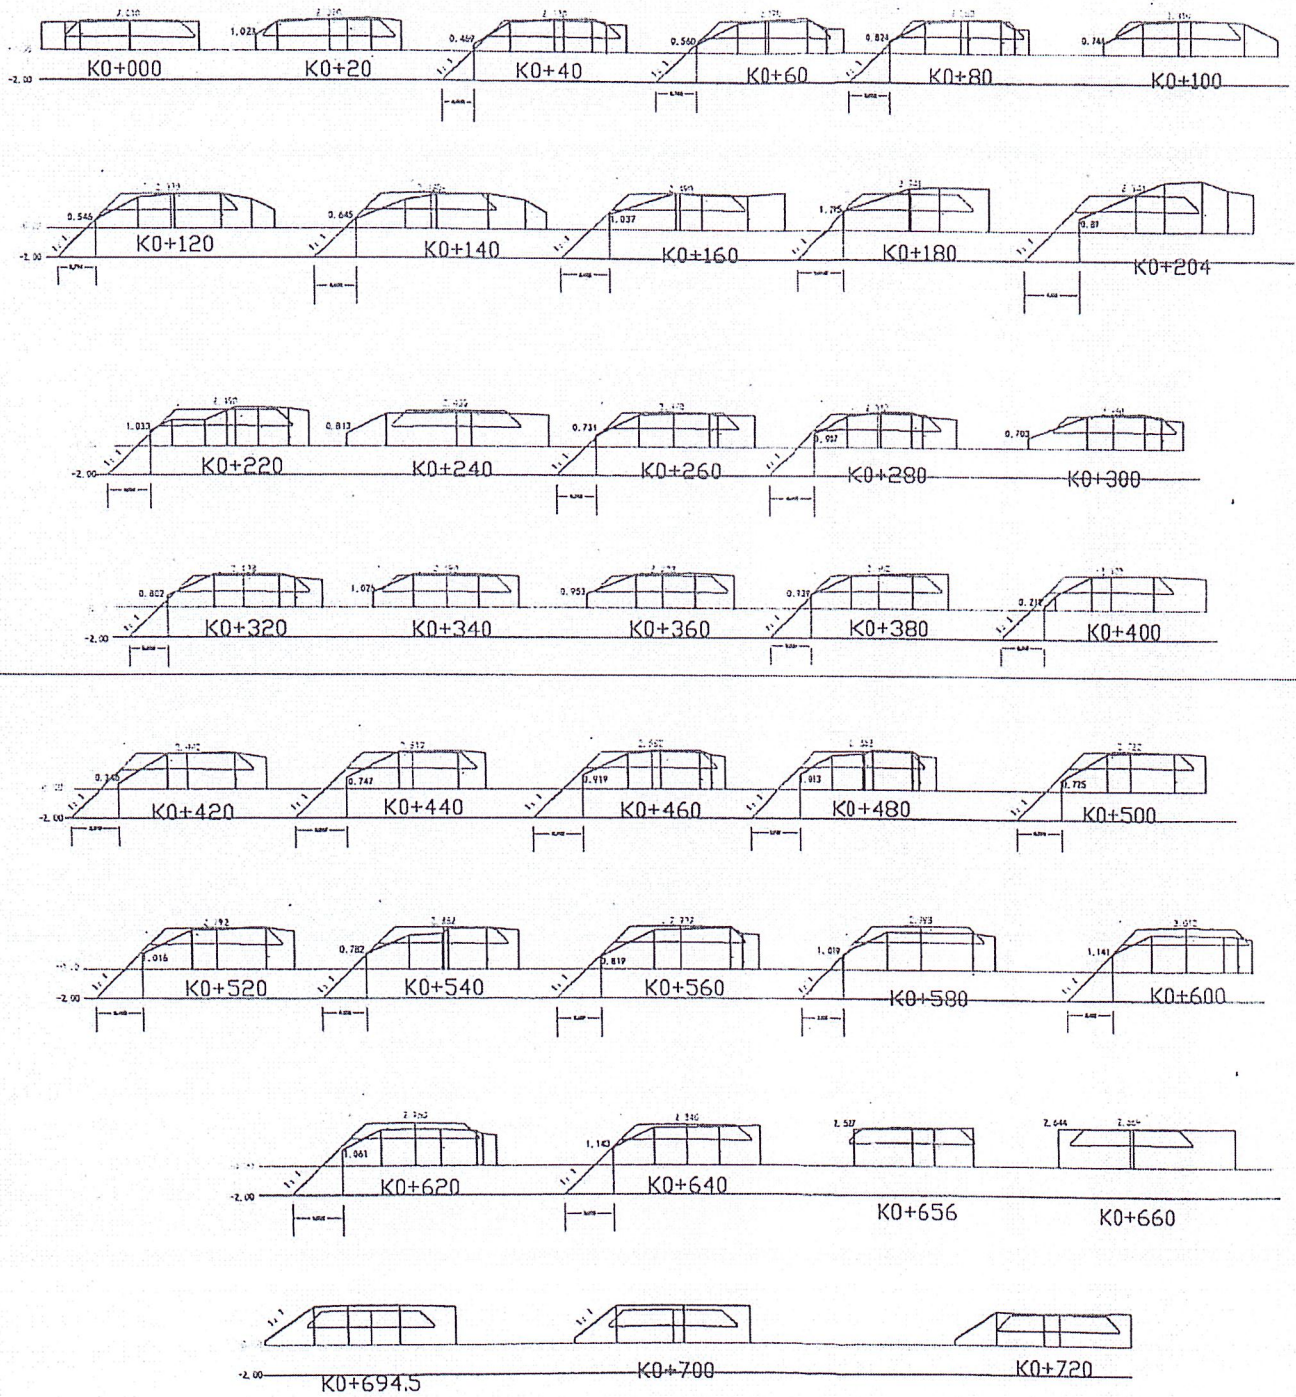

沃港路临河侧现场调查数据

点名	路基边桩设计高程 (偏距3米)/m	原槽边桩高程 (偏距4.41米) /m	水面高程/m	淤泥顶高程 /m	淤泥底高程 /m	路基边桩顶到 水面高差/m	原槽边桩顶到 水面高差/m	淤泥厚度/m
K0+044.217	2.098	1.137	0.700	-0.036	-0.467	1.398	0.437	0.431
K0+072.325	2.182	1.221	0.700	-0.149	-0.420	1.482	0.521	0.271
K0+139.260	2.383	1.422	0.700	0.250	-0.359	1.683	0.722	0.609
K0+261.996	2.319	1.358	0.700	0.223	-0.309	1.619	0.658	0.532
K0+353.944	2.169	1.208	0.700	0.170	-0.394	1.469	0.508	0.564
K0+393.516	2.305	1.344	0.700	0.115	-0.479	1.605	0.644	0.594
K0+457.324	2.528	1.567	0.700	0.187	-0.413	1.828	0.867	0.600
K0+488.171	2.636	1.675	0.700	0.139	-0.373	1.936	0.975	0.512
K0+637.274	2.815	1.854	0.700	0.176	-0.337	2.115	1.154	0.513
K0+710.724	2.179	1.218	0.700	0.086	-0.258	1.479	0.518	0.344

射阳县农村公路2025年建设工程（二标） 沃港路原地面高程测量数据

序号	里程	偏距	高程(H)	备注
1	K0+000.083	0.073	1.955	
2	K0+000.199	-3.523	1.881	
3	K0+020.287	4.924	2.002	
4	K0+021.341	3.203	2.206	
5	K0+020.074	1.246	2.149	
6	K0+021.375	-3.437	1.903	
7	K0+021.812	-4.908	1.023	
8	K0+040.015	4.959	1.868	
9	K0+040.554	3.696	1.863	
10	K0+040.534	2.665	2.276	
11	K0+040.369	0.687	2.219	
12	K0+036.513	-2.230	1.988	
13	K0+036.652	-5.070	0.469	
14	K0+060.099	5.648	1.623	
15	K0+060.098	4.262	1.697	
16	K0+059.822	2.934	2.353	
17	K0+059.914	-0.275	2.216	
18	K0+059.863	-2.268	1.963	
19	K0+059.911	-5.123	0.56	
20	K0+079.575	4.865	1.681	
21	K0+079.388	3.862	1.677	
22	K0+079.417	2.872	2.321	
23	K0+080.038	0.510	2.249	
24	K0+080.026	-2.576	2.114	
25	K0+079.848	-5.097	0.824	
26	K0+100.397	7.216	1.128	
27	K0+100.267	4.813	2.208	
28	K0+100.292	0.904	2.333	
29	K0+100.059	-2.566	2.176	
30	K0+100.374	-5.407	0.744	
31	K0+120.540	7.103	1.264	

注明：偏距右偏为正数，左偏为负数。

测量：颜青涛

复核：王国峰

现场监理：何飞

2025.7.14

射阳县农村公路2025年建设工程（二标） 沃港路原地面高程测量数据

序号	里程	偏距	高程(H)	备注
32	K0+120.609	5.471	1.971	
33	K0+120.873	3.412	2.365	
34	K0+120.594	0.244	2.319	
35	K0+120.572	-2.244	2.072	
36	K0+120.725	-5.349	0.546	
37	K0+139.351	8.032	1.111	
38	K0+139.276	6.546	1.981	
39	K0+139.189	3.958	2.401	
40	K0+139.028	0.367	2.321	
41	K0+139.195	-1.865	1.946	
42	K0+139.107	-5.268	0.645	
43	K0+160.742	7.464	2.545	
44	K0+160.780	4.625	2.385	
45	K0+160.527	1.477	2.41	
46	K0+160.604	-0.362	2.526	
47	K0+160.923	-4.862	1.037	
48	K0+180.016	5.687	2.927	
49	K0+179.870	2.068	2.962	
50	K0+180.177	-0.109	2.856	
51	K0+180.619	-4.827	1.295	
52	K0+204.227	7.338	2.605	
53	K0+204.254	5.483	2.865	
54	K0+204.196	3.611	3.497	
55	K0+205.421	0.999	3.363	
56	K0+204.411	-5.354	0.89	
57	K0+220.564	5.621	2.363	
58	K0+220.423	4.223	2.589	
59	K0+220.450	2.146	2.661	
60	K0+220.165	0.620	2.662	
61	K0+220.377	-1.469	1.767	
62	K0+220.865	-3.737	1.788	

注明：偏距右偏为正数，左偏为负数。

测量：颜青珂

复核：王国辉

现场监理：何飞

2025.7.14

射阳县农村公路2025年建设工程（二标）
沃港路原地面高程测量数据

序号	里程	偏距	高程(H)	备注
63	K0+220.912	-5.231	1.033	
64	K0+240.616	6.436	2.136	
65	K0+240.227	1.045	2.306	
66	K0+247.922	-2.315	2.169	
67	K0+248.374	-5.425	0.813	
68	K0+260.512	5.620	2.153	
69	K0+260.393	3.086	2.141	
70	K0+260.431	2.481	2.319	
71	K0+260.748	-2.386	2.157	
72	K0+261.127	-5.345	0.731	
73	K0+281.876	5.357	2.004	
74	K0+281.814	2.937	2.13	
75	K0+281.550	2.092	2.421	
76	K0+281.303	-0.071	2.403	
77	K0+281.840	-2.478	2.115	
78	K0+282.100	-4.929	0.907	
79	K0+300.920	4.947	1.923	
80	K0+300.772	3.407	2.052	
81	K0+300.806	2.189	2.388	
82	K0+301.140	-2.065	2.218	
83	K0+304.304	-5.919	0.703	
84	K0+320.195	5.364	1.872	
85	K0+320.132	3.545	2.026	
86	K0+320.152	2.452	2.298	
87	K0+320.270	-2.035	2.242	
88	K0+320.497	-5.231	0.802	
89	K0+340.115	5.052	2.167	
90	K0+339.945	2.201	2.299	
91	K0+340.200	-2.343	2.244	
92	K0+340.780	-5.142	1.026	
93	K0+359.629	4.986	2.256	

注明：偏距右偏为正数，左偏为负数。

测量：颜青萍

复核：王同辉

现场监理：何飞

2025.7.14

**射阳县农村公路2025年建设工程（二标）
沃港路原地面高程测量数据**

序号	里程	偏距	高程(H)	备注
94	K0+359.523	2.288	2.383	
95	K0+359.503	-1.848	2.279	
96	K0+359.027	-5.192	0.953	
97	K0+380.191	4.997	2.419	
98	K0+380.229	2.382	2.415	
99	K0+380.014	-1.863	2.232	
100	K0+381.099	-4.910	0.939	
101	K0+400.523	6.862	2.218	
102	K0+400.220	3.117	2.377	
103	K0+400.557	-1.515	2.265	
104	K0+401.129	-4.183	0.961	
105	K0+401.331	-4.990	0.212	
106	K0+420.381	5.413	2.152	
107	K0+420.445	3.273	2.457	
108	K0+420.686	-1.328	2.382	
109	K0+420.652	-4.841	0.346	
110	K0+440.979	5.042	2.468	
111	K0+440.468	3.190	2.614	
112	K0+440.630	-1.077	2.515	
113	K0+439.696	-4.700	0.747	
114	K0+461.051	4.987	2.235	
115	K0+460.897	4.042	2.37	
116	K0+460.945	3.239	2.68	
117	K0+460.461	0.541	2.704	
118	K0+460.615	-1.763	2.389	
119	K0+460.736	-4.938	0.919	
120	K0+480.527	5.301	2.271	
121	K0+480.403	4.060	2.369	
122	K0+480.467	3.531	2.683	
123	K0+480.472	0.792	2.722	
124	K0+480.500	0.111	2.429	

注明：偏距右偏为正数，左偏为负数。

测量：张永强

复核：王国锋

现场监理：何飞

2025.7.14

射阳县农村公路2025年建设工程（二标）
沃港路原地面高程测量数据

序号	里程	偏距	高程(H)	备注
125	K0+480.650	-2.234	2.319	
126	K0+480.849	-4.688	1.013	
127	K0+500.883	5.350	2.519	
128	K0+500.860	3.099	2.67	
129	K0+500.812	-1.819	2.545	
130	K0+501.136	-5.252	0.725	
131	K0+520.063	5.332	2.554	
132	K0+519.863	3.367	2.813	
133	K0+520.013	-1.768	2.608	
134	K0+520.944	-5.085	1.016	
135	K0+540.564	5.215	2.654	
136	K0+540.688	3.000	2.805	
137	K0+540.481	0.271	2.716	
138	K0+540.277	-0.136	2.405	
139	K0+540.228	-2.488	2.247	
140	K0+539.305	-5.453	0.782	
141	K0+560.149	-5.643	0.819	
142	K0+560.247	-1.917	2.612	
143	K0+560.895	3.361	2.818	
144	K0+560.938	4.238	2.414	
145	K0+561.058	5.360	2.343	
146	K0+581.137	5.237	2.302	
147	K0+581.848	3.820	2.535	3.828. 2.57
148	K0+582.014	-2.445	2.576	
149	K0+582.321	-5.722	1.019	
150	K0+600.463	-5.438	1.141	-
151	K0+600.487	-2.538	2.494	-2.53. 2.56
152	K0+600.429	2.663	2.434	
153	K0+600.595	3.694	2.353	
154	K0+600.713	4.701	2.196	
155	K0+620.916	5.645	2.063	

注明：偏距右偏为正数，左偏为负数。

测量：颜青峰

复核：王同峰

现场监理：何飞

2025.7.14

射阳县农村公路2025年建设工程（二标） 沃港路原地面高程测量数据

序号	里程	偏距	高程(H)	备注
156	K0+620.936	4.676	2.174	
157	K0+621.034	4.265	2.403	
158	K0+620.988	1.728	2.539	
159	K0+620.934	-2.490	2.455	
160	K0+620.946	-5.242	1.061	-5.26-1.08
161	K0+640.826	5.092	2.756	
162	K0+640.843	2.231	2.658	
163	K0+640.599	-2.361	2.593	
164	K0+640.692	-5.275	1.143	
165	K0+657.143	3.393	2.674	
166	K0+656.651	0.612	2.595	
167	K0+655.333	-4.936	2.527	
168	K0+660.204	7.586	2.663	
169	K0+658.749	0.388	2.642	
170	K0+657.640	-5.175	2.644	
171	K0+694.938	6.006	2.619	
172	K0+694.935	2.038	2.711	
173	K0+694.794	-1.660	2.696	
174	K0+694.882	-4.064	2.615	
175	K0+695.225	-7.506	0.312	
176	K0+700.428	5.410	2.575	
177	K0+699.964	0.792	2.615	
178	K0+700.299	-4.012	2.568	
179	K0+700.191	-6.946	0.383	
180	K0+720.161	5.380	2.268	
181	K0+719.506	-1.127	2.164	
182	K0+717.401	-4.196	2.318	
183	K0+716.805	-7.221	0.374	

注明：偏距右偏为正数，左偏为负数。

测量：颜青海

复核：王同峰

现场监理：何飞

2025.7.14
